

Exam Questions PK0-005

CompTIA Project+ Certification Exam

<https://www.2passeasy.com/dumps/PK0-005/>



NEW QUESTION 1

Following a successful release, a project manager sent a survey to all stakeholders to gain an understanding of opportunity areas for the team. Which of the following can use the survey results as an input?

- A. Daily stand-up
- B. Project momentum
- C. Performance feedback
- D. Meeting minutes

Answer: B

NEW QUESTION 2

Which of the following BEST describes how an organization should coordinate management of multiple related projects?

- A. Apply the SDLC process.
- B. Establish a program.
- C. Consult the CCB.
- D. Use different frameworks.

Answer: B

NEW QUESTION 3

A project manager realizes that a project will not be completed on time due to resource constraints. Which of the following actions should the project manager take NEXT?

- A. Trigger the contingency plan and communicate with the stakeholders.
- B. Work with the functional managers to create a work-around.
- C. Submit a change request to the change control board.
- D. Transfer the risk by hiring a new vendor who was successful on a previous project.
- E. Set up an escalation meeting with the sponsor.

Answer: A

NEW QUESTION 4

A PM has identified all the resources involved in a project. The next step is to identify which resources are responsible for which tasks. Which of the following should be used to document this information?

- A. RFI
- B. RACI
- C. WBS
- D. SOW

Answer: B

NEW QUESTION 5

Which of the following should occur when implementing an IT infrastructure change that takes risks into consideration?

- A. Approving the change request
- B. Developing a rollback plan
- C. Gathering necessary resources
- D. Defining requirements

Answer: B

NEW QUESTION 6

A project manager was not part of a contract negotiation. The project manager is concerned that stakeholders will expect the project to achieve deliverables requested in the RFP. Which of the following documents should the project manager produce FIRST to start communication about the boundaries of the project?

- A. Milestone chart
- B. Work breakdown structure
- C. Project charter
- D. Detailed scope statement

Answer: C

NEW QUESTION 7

A third party needs to perform a short-term task for which the duration cannot be accurately estimated and the cost cannot be calculated in advance. Which of the following should the project manager put in place before work begins?

- A. Time and materials contract
- B. Master service agreement
- C. Fixed-price contract
- D. Statement of work
- E. Cost-plus agreement

Answer: A

NEW QUESTION 8

While developing a project charter, a PM discovers that some of the legal requirements have not been addressed during the project concept preparation, which could result in significant financial penalties against the organization. The PM knows that implementation of appropriate changes is costly and will exceed the budget and scope of the project. Which of the following should the PM do FIRST?

- A. Escalate the finding to the change control board.
- B. Add a risk to the risk register for validation.
- C. Consult the RACI matrix to identify ownership of the risk.
- D. Have a meeting with the project sponsor and main stakeholders.

Answer: D

NEW QUESTION 9

A company that is implementing an updated version of its main product hired a new project manager to lead the project. Prior to the start of the project, the sponsor asked the project manager to prepare a report on the defects found in the previous project to avoid a decrease in production. The report shows that the two main defects are related to cosmetic and physical damage to the product. Which of the following charts would BEST prioritize which defects to address?

- A. Pareto
- B. Run
- C. Control
- D. Histogram

Answer: A

NEW QUESTION 10

A project manager sent equipment to a global project team for testing purposes. Only 70% of the project team received the equipment for testing. Which of the following considerations is impacting the rest of the team?

- A. Quality assurance
- B. Organizational branding restrictions
- C. State privacy acts
- D. Country legal regulations

Answer: D

NEW QUESTION 10

A project manager has been assigned to a new project. During the planning phase, the project manager needs to get an understanding of the purpose of the project. Which of the following should the project manager do?

- A. Collate the lessons learned.
- B. Perform a gap analysis.
- C. Review existing artifacts.
- D. Conduct a retrospective.

Answer: C

NEW QUESTION 12

Due to multiple changes, the sign-off for the project scope baseline is delayed. The project sponsor has restricted the budget for this project. Which of the following should the project manager MOST likely do to move forward?

- A. Communicate with the affected stakeholders.
- B. Initiate a formal change request to modify the cost.
- C. Adjust the scope to stay within the cost.
- D. Set a new cost using a lightweight estimation method.

Answer: C


NEW QUESTION 16

As a result of an approved change, the project manager updates the project plan with the newest project end date. Which of the following change control processes should the project manager complete NEXT?

- A. Document the request in the change control log.
- B. Communicate the change deployment.
- C. Conduct an impact assessment.
- D. Implement the change.

Answer: C

Explanation:

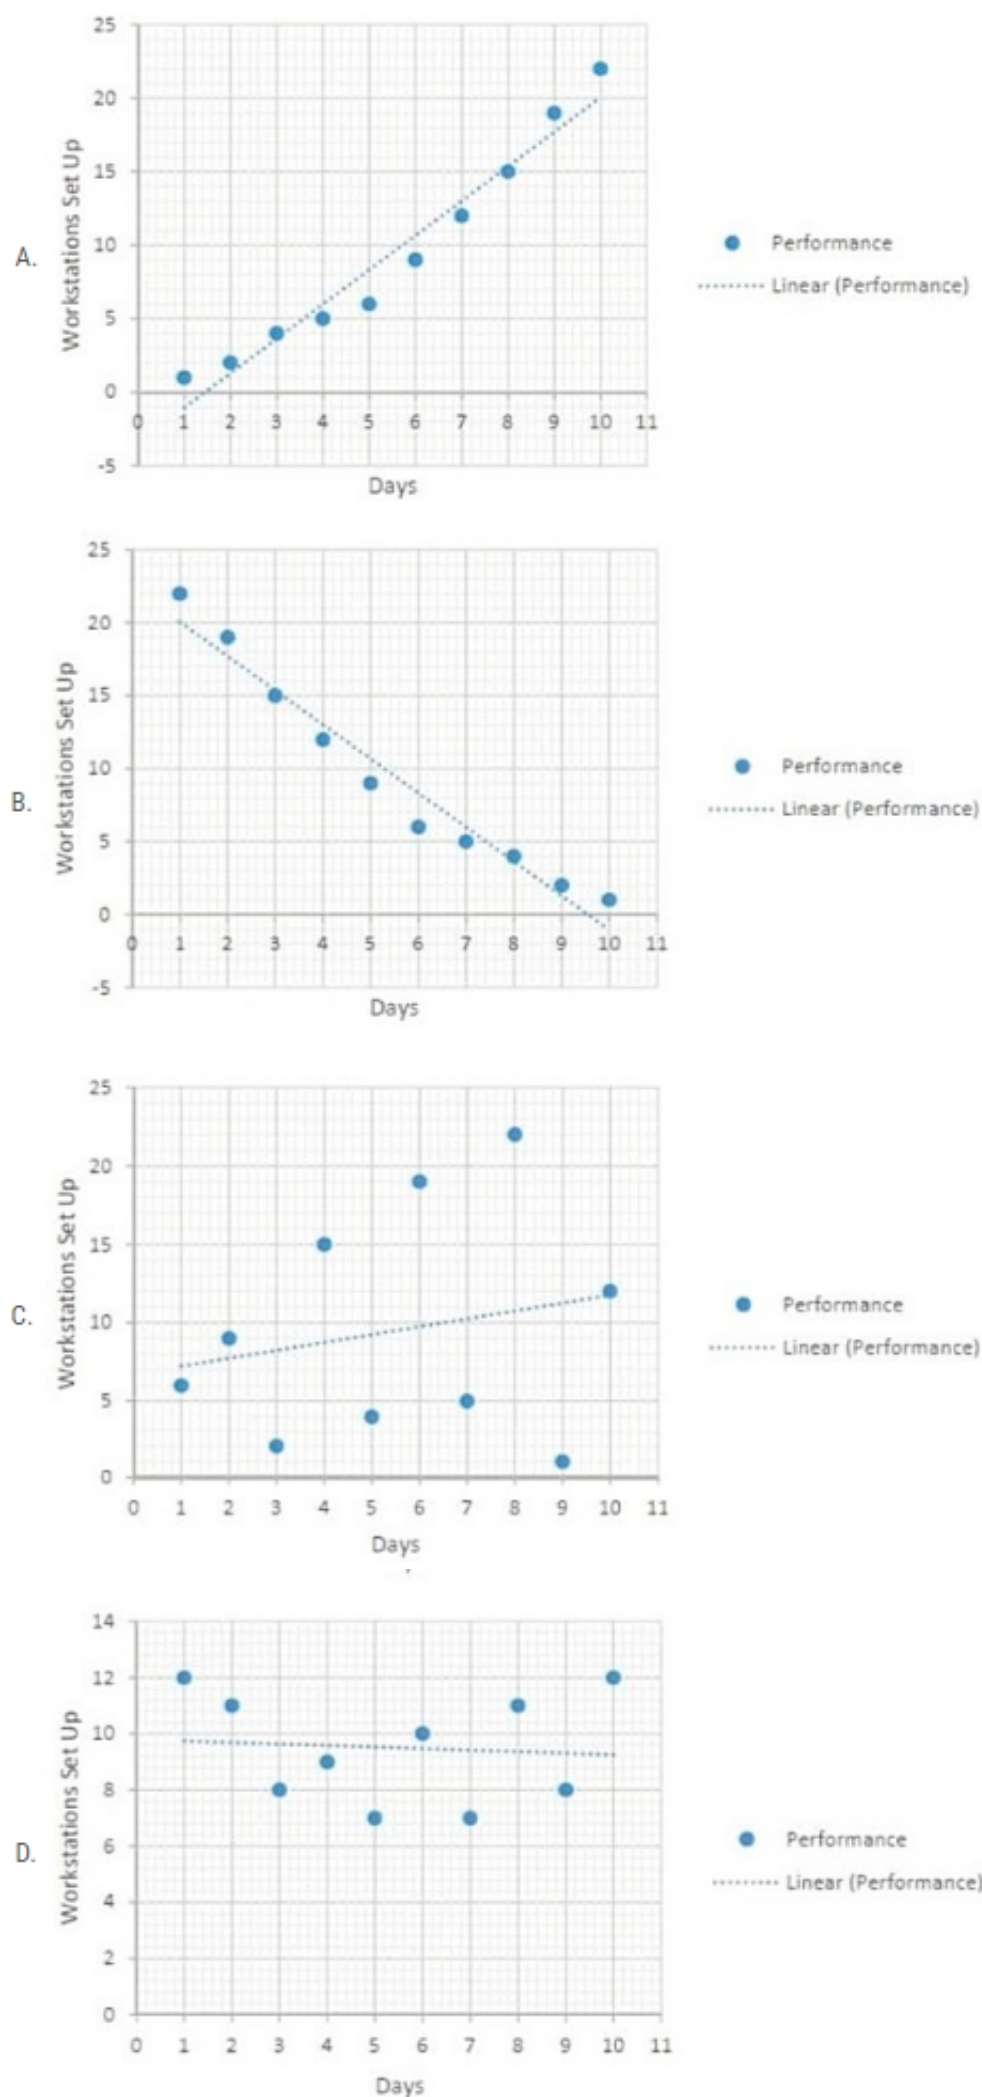

NEW QUESTION 20

An opportunity emerged in the middle of a project life cycle. Which of the following is the BEST action for the project manager to take?

- A. Exploit the risk.
- B. Accept the risk.
- C. Avoid the risk.
- D. Transfer the risk.

Answer: D

NEW QUESTION 24

A project manager was just assigned to a new project. Which of the following activities should the project manager undertake after accepting the project? (Choose two.)

- A. Review the detailed plan.
- B. Develop a preliminary scope.
- C. Develop a transition plan.
- D. Develop a project management plan.

- E. Review the resource pool.
- F. Review the project objectives.

Answer: AF

NEW QUESTION 27

A program manager is reviewing the project portfolio and prioritizing each project based on the company's strategic plan. Which of the following should be considered in this evaluation? (Choose two.)

- A. Company vision
- B. Global environment
- C. Brand value
- D. Mission statement
- E. Portfolio budget
- F. Local legislation

Answer: AB

NEW QUESTION 32


Halfway through a project, the sponsor states that the project is taking too long to complete. Which of the following should the project manager consult?

- A. Gantt chart
- B. Maintenance window schedule
- C. Functional requirements
- D. Test results

Answer: A

NEW QUESTION 33

During a brainstorming session, a project team is elaborating on what caused the unexpected crash of the website that the team was developing. Given the following:

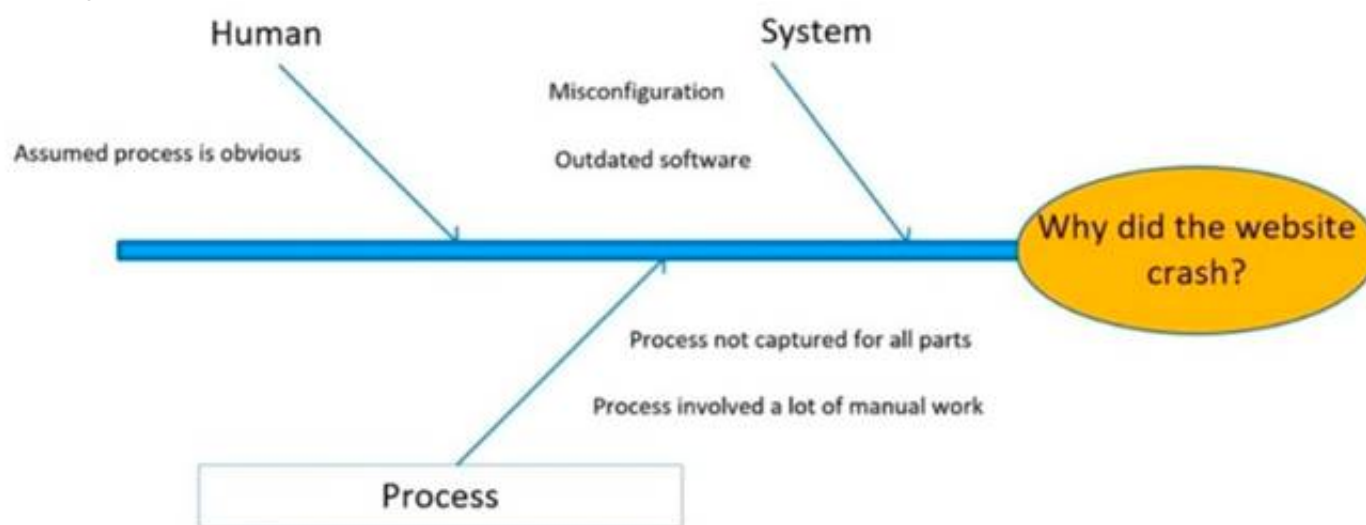

the issue?

Which of the following was the initial cause of

- A. Inadequate memory
- B. Incorrect configuration
- C. Lack of infrastructure
- D. Inadequate instructions

Answer: B

NEW QUESTION 36

Which of the following describes three-tier architecture?

- A. Conceptual, design, and implementation stages
- B. Presentation, application, and data processing
- C. Network, software, and security
- D. Development, testing, and production environment

Answer: B

NEW QUESTION 41

.....

THANKS FOR TRYING THE DEMO OF OUR PRODUCT

Visit Our Site to Purchase the Full Set of Actual PK0-005 Exam Questions With Answers.

We Also Provide Practice Exam Software That Simulates Real Exam Environment And Has Many Self-Assessment Features. Order the PK0-005 Product From:

<https://www.2passeasy.com/dumps/PK0-005/>

Money Back Guarantee

PK0-005 Practice Exam Features:

- * PK0-005 Questions and Answers Updated Frequently
- * PK0-005 Practice Questions Verified by Expert Senior Certified Staff
- * PK0-005 Most Realistic Questions that Guarantee you a Pass on Your FirstTry
- * PK0-005 Practice Test Questions in Multiple Choice Formats and Updatesfor 1 Year
